Project Schedule

138 kV Springwoods Project Schedule
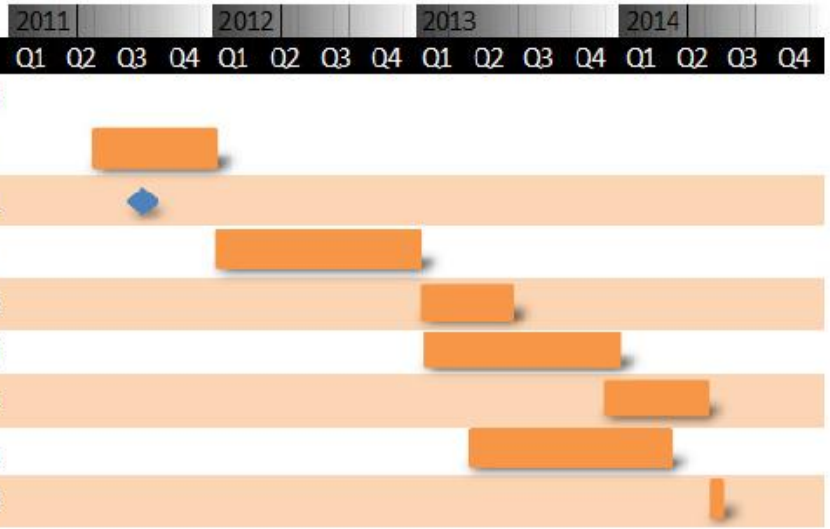
TASK NAME	DURATION	START	FINISH
138 kV Springwoods Project	**160 weeks**	**06.01.11**	**06.29.14**
CCN Application Preparation	32 weeks	06.01.11	1.12.12
Public Meeting	1 Day	09.06.11	09.06.11
CCN Application Review & Approval (PUCT)	52 weeks	1.12.12	1.14.13
Project Surveying & Abstracting	24 weeks	1.14.13	06.27.13
Right of Way Acquisition	50 weeks	1.14.13	12.31.13
Transmission Construction	28 weeks	12.01.13	06.15.14
Substation Construction	52 weeks	04.01.13	04.01.14
Substation Commissioning	2 weeks	06.15.14	06.29.14
